

PURAVANKARA



A
PURAVANKARA HOME AT
PURVA PARK HILL

Pride of owning something precious

PURVA PARK HILL

Construction Updates

January 2025

Dear Esteemed Customer,


Greetings from Puravankara

It gives us immense pleasure to update you through this edition of Puravankara Newsletter and provide you with the latest information about your home in Purva Park Hill. As we move ahead, we at Puravankara sincerely thank you for your continual faith and trust reposed in the brand.

We are happy to inform you that the construction and infrastructure works at the site is progressing well. We thank you for your understanding that is a construction site with extensive debris, heavy vehicular movement, uneven surfaces and hence keeping in mind your safety, visits to this site is restricted. You may seek prior approval and we can accommodate the scheduled visit from your respective banker.

We are grateful for your kind cooperation.

Team Purva Park Hill

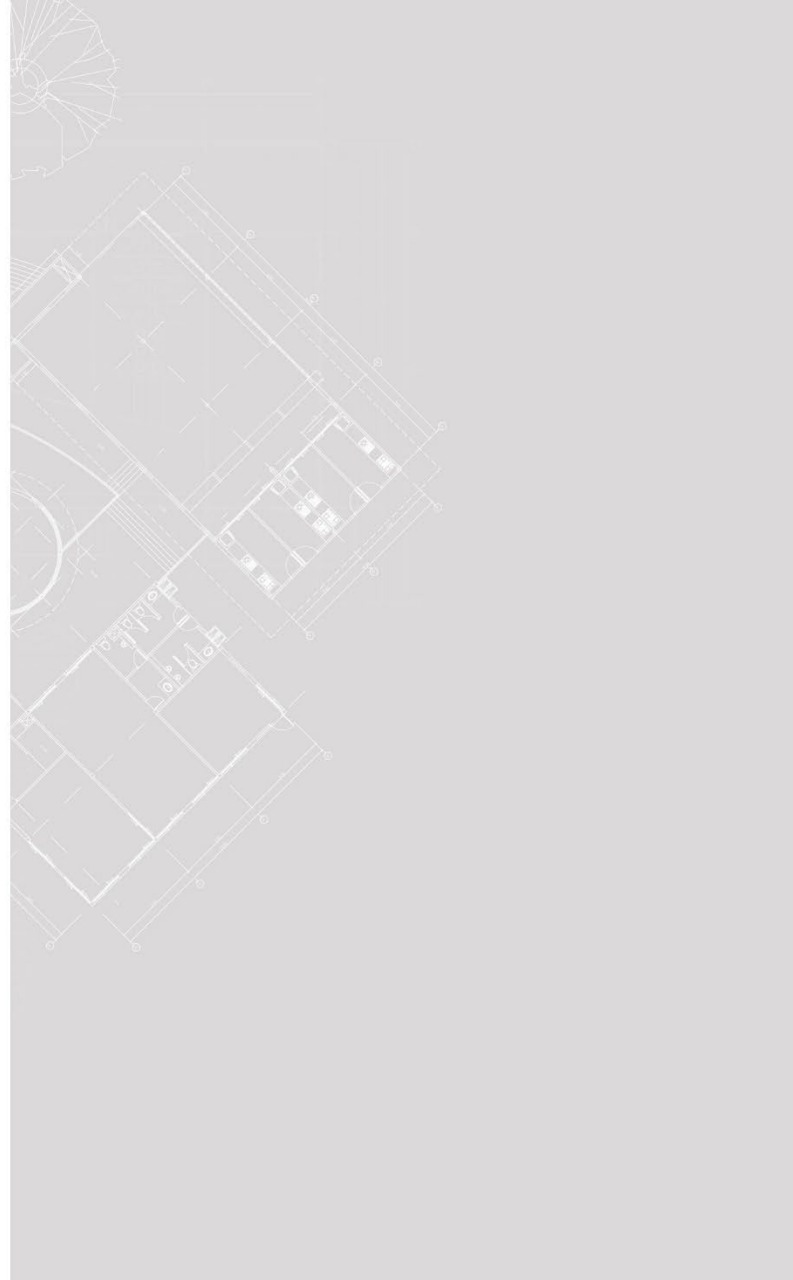



Purva Park Hill

Off Kanakapura Road, Bengaluru



Construction Updates

Overall view

Tower A



Actual site photograph

TOWER STATUS

- Above terrace works in progress.
- Up to 18th block work completed.
- Up to 17th floors plastering works completed.
- Up to 14th floors waterproofing works completed.
- Up to 18th floors electrical conduit works in completed.
- Up to 10th floor FPS works in progress.
- Up to 18th floor railing works in progress.
- Up to 13th plumbing works in progress.
- Painting works in progress.
- 7th & 8th floor tile works in progress.



MILESTONES ACHIEVED

- Terrace slab concrete completed.
- 4th, 5th & 6th floor tile works completed.



UPCOMING MILESTONES

- 7th, 8th & 9th floor tile works completion.

PROGRESS TIMELINE



October 24

November 24

December 24

January 25

Tower B



Actual site photograph

TOWER STATUS

- Terrace floor slab completed.
- Above terrace floor slab works in progress.
- Block works completed up to 17th floor.
- Up to 14th floor floors plastering works completed.
- Up to 9th floor waterproofing works in completed.
- Up to 14th floor electrical works completed.
- FPS works in progress.
- 8th & 9th floor plumbing works in progress.
- Up to 15th floor railing works completed.



MILESTONES ACHIEVED

- 18th floor slab completed.
- Terrace floor slab completed.



UPCOMING MILESTONES

- 7th & 8th floor tiling works completion.

PROGRESS TIMELINE



October 24

November 24

December 24


January 25

Tower C



Actual site photograph

PROGRESS TIMELINE



October 24

November 24

December 24

January 25

TOWER STATUS

- Above terrace work completed.
- Terrace waterproofing – 100% completed.
- UPVC – 100% completed.
- Tiling works : 100% completed.
- Lobby false ceiling works completed.
- Internal painting works in progress.
- Staircase & balcony railing works completed.
- FPS works : Ground floor to 20th floor completed.
- Lift works in progress.
- External painting works in progress.
- Entrance portal works in progress
- Wooden door installation is in progress.



MILESTONES ACHIEVED

- Structure completed.
- Ground floor to 20th floor tile completed.



UPCOMING MILESTONES

- 8th, 9th, 11th to 12th floor doors and windows.

Tower D



Actual site photograph



TOWER STATUS

- UPVC 100% floor completed.
- Plumbing works 100% completed.
- Tiling works : 100% completed.
- Balcony & staircase railing works : completed.
- FPS works; completed.
- Internal painting works in progress.
- Lift works completed.
- Lobby works in progress.
- External painting works in progress.
- Door fixing woks in progress
- CP & sanitary fixing in progress.
- Plumbing testing works in progress.
- Entrance portal works in progress.
- Terrace finishing works in progress.



MILESTONES ACHIEVED

- 2nd, 3rd, 4th, 5th, 6th, 7th, 8th, 9th, 11th, 17th, 18th & 19th floor doors & windows fixing completed.
- 7th & 8th floor CP & sanitary fixing completed.



UPCOMING MILESTONES

- 1st, 10th , 14th, 15th & 20th floor doors & windows completion.

PROGRESS TIMELINE



October 24

November 24

December 24

January 25

External development



Actual site photograph

TOWER STATUS

- Amphitheatre finishing works in progress.
- Put-put golf, pet activity, climbing wall & multi court areas back filling works in progress.
- Podium ramp works in progress.
- Basement ramps works completed.
- Yoga deck works completed.
- Multi court ramp works completed.
- Multi court fencing works in progress.
- Podium planter works in progress.
- Fire driveway works in progress.
- External waterproofing in progress
- Compound wall works in progress.
- Basement works in progress.
- Pump room works in progress.
- External painting works in progress.
- External plumbing and electrical works in progress.
- External fire fighting works in progress.

PROGRESS TIMELINE



October 24

November 24

December 24

January 25

Contact us

Site Office :

Purva Park Hill

Off, Kanakapura Rd, Mallasandra, Bengaluru – 560062

Regional Office :

Puravankara Limited. #130/1, Ulsoor Road,
Bengaluru - 560 042

Email : crm@puravankara.com (Subject line – Project name/ unit number)

Call Us : +91 - 80-67724001 / 1 860 208 0000

Web : www.puravankara.com

RERA Registration Number :

RERA NO: PRM/KA/RERA/1251/310/PR/220601/004946/47/48/49
