


PURAVANKARA

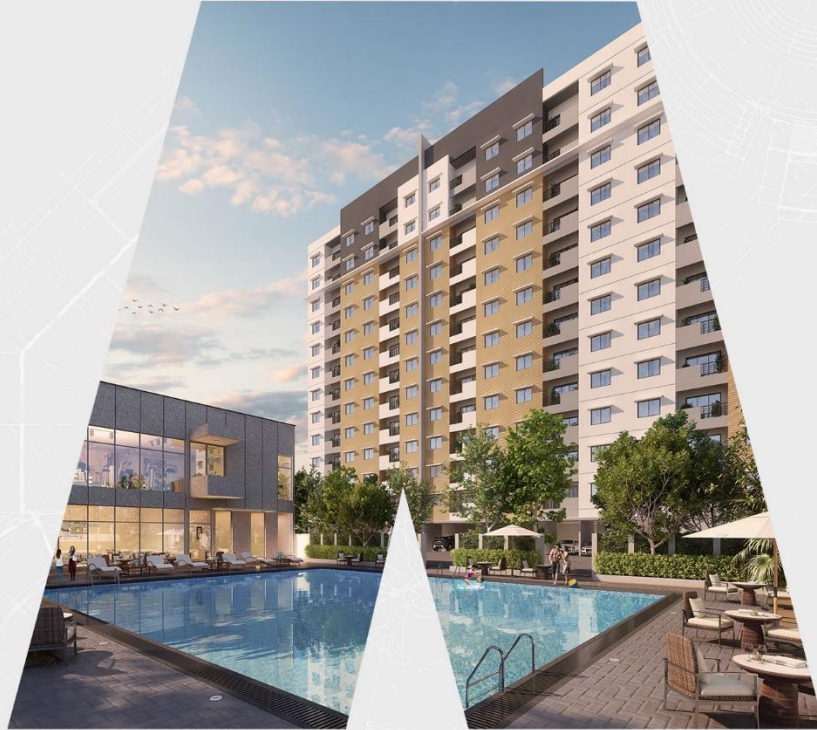

A
PURAVANKARA HOME AT
LAKEVISTA

Pride of owning something precious

LAKEVISTA
— AT —
PURVA
WINDERMERE
PALLIKARANAI

Construction Updates

May 2026

Dear Esteemed Customer,


Greetings from Puravankara

It gives us immense pleasure to update you through this edition of Puravankara Newsletter and provide you with the latest information about your home in Lakevista. As we move ahead, we at Puravankara sincerely thank you for your continual faith and trust reposed in the brand.

We are happy to inform you that the construction and infrastructure works at the site is progressing well. We thank you for your understanding that is a construction site with extensive debris, heavy vehicular movement, uneven surfaces and hence keeping in mind your safety, visits to this site is restricted. You may seek prior approval and we can accommodate the scheduled visit from your respective banker.

We are grateful for your kind cooperation.

Team Lakevista

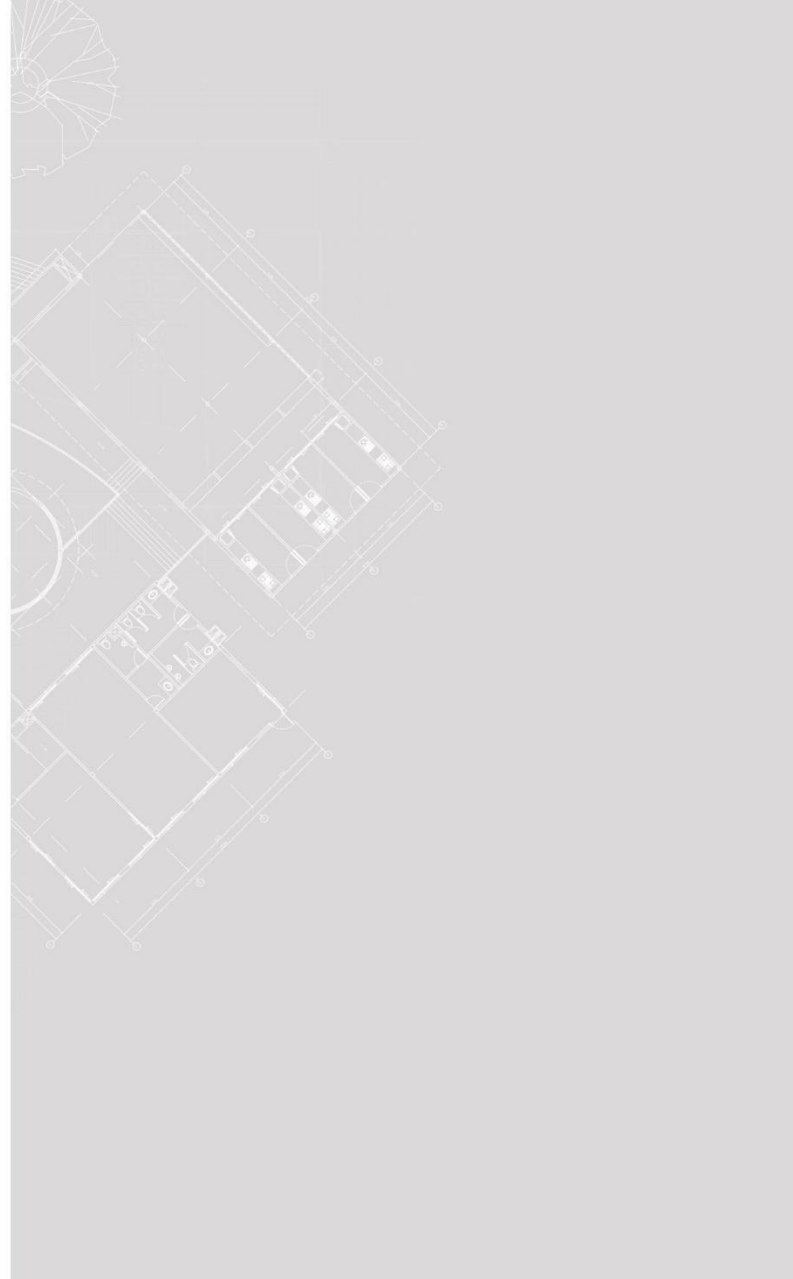



Lakevista

Pallikaranai, Chennai



Construction Updates

Overall view



Tower K

TOWER STATUS

- Structure Completed.
- Tiling Completed.
- 7th, 8th & 9th Floor Windows & Door Installation in Progress.
- 1st to 5th Floor Internal Painting in Progress.
- External Texture and External Painting works in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Structure Completed.
- Tiling Completed.
- Doors & Windows Completed till 6th Floor.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Doors & Windows till 9th Floor.
- Completion of Exterior Texture & Painting.
- Completion of painting works till 5th Floor.

PROGRESS TIMELINE



October 25



November 25



December 25



January 26



February 26



March 26



April 26

Tower M3



TOWER STATUS

- Tiling works completed.
- Joinery Completed.
- Exterior Texture and Painting in Progress.
- Internal Painting 1st Coat completed.
- 10th Floor CP & Sanitary Installation in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Structure Completed.
- Tiling Completed.
- Joinery completed.
- CP & Sanitary installation till 4th Floor.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Exterior Texture and Painting.
- CP & Sanitary Installation till 11th Floor.
- Completion of Internal 2nd Coat painting.

PROGRESS TIMELINE



Tower M2



TOWER STATUS

- Structure Completed.
- Internal Gypsum Plaster Completed.
- 5th to 7th Floor Tiling in Progress.



CONSTRUCTION MILESTONES ACHIEVED


- Structure Completed.
- Tiling Completed till 4th Floor.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Tiling till 8th Floor.
- Completion of Doors & Windows till 3rd Floor.

PROGRESS TIMELINE



Tower M1



TOWER STATUS

- Structure Completed.
- Internal Gypsum Plaster Completed.
- 11th Floor Tiling in Progress.
- 5th to 7th Floor Doors & Windows in Progress.
- Exterior Texture and Painting in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Structure Completed.
- Tiling Completed.
- Doors & Windows Completed till 5th Floor.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Doors & Windows till 8th Floor.
- Completion of Exterior Texture & Painting.

PROGRESS TIMELINE



October 25



November 25



December 25



January 26



February 26



March 26



April 26

Tower P4



TOWER STATUS

- Structure Completed.
- Internal Gypsum Plaster Completed.
- Tiling Works Completed.
- Windows installation progress in 7th to 10th Floor & Doors in 6th Floor.
- Exterior Texture & Painting in Progress.



CONSTRUCTION MILESTONES ACHIEVED


- Structure Completed.
- Tiling works Completed.
- Doors & Windows till 5th Floor Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Doors & Windows till 8th Floor.
- Completion of Exterior Texture & Painting.

PROGRESS TIMELINE



October 25

November 25

December 25

January 26

February 26

March 26

April 26

Tower E15



TOWER STATUS

- Structure Completed.
- Internal Plaster Completed.
- 10th Floor Tiling in Progress.
- Exterior Texture & painting in Progress.
- Doors & Windows installation progress.



CONSTRUCTION MILESTONES ACHIEVED

- Structure Completed.
- Internal & External Plaster Completed.
- Tiling till 09th Floor Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Tiling.
- Completion of Exterior Texture & Painting.
- Completion of Doors & Windows till 3rd Floor.

PROGRESS TIMELINE



October 25



November 25



December 25



January 26



February 26



March 26



April 26

Tower P3



TOWER STATUS

- Structure Completed.
- 10th Floor Internal Gypsum Plaster in Progress.
- 1st to 4th Floor Tiling in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Structure Completed.
- Internal Gypsum Plaster Completed till 9th Floor.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Internal Gypsum Plaster till 11th Floor.
- Completion of Tiling till 3rd Floor.

PROGRESS TIMELINE



October 25

November 25

December 25

January 26

February 26

March 26.

April 26

Tower L



TOWER STATUS

- Structure Completed.
- 6th Floor Internal Gypsum Plaster in Progress.
- 1st to 4th Floor Tiling in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Structure Completed.
- Internal Gypsum Plaster till 5th Floor Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Internal Gypsum Plaster till 7th Floor.
- Completion of Tiling till 3rd Floor.

PROGRESS TIMELINE



October 25



November 25



December 25



January 26



February 26



March 26



April 26



Tower P2

TOWER STATUS

- Structure Completed
- 6th Floor Internal Gypsum Plaster in Progress.
- 1st & 2nd Floor Tiling in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Structure Completed.
- Internal Gypsum Plaster till 5th Floor Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Gypsum Plaster till 08th Floor.
- Completion of Floor Tiling till 2nd Floor.

PROGRESS TIMELINE



October 25



November 25



December 25



January 26



February 26



March 26



April 26



Tower M4

TOWER STATUS

- 7th Floor Slab works in progress.



CONSTRUCTION MILESTONES ACHIEVED

- 6th Floor Slab Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of 7th Floor Slab.

PROGRESS TIMELINE



October 25



November 25



December 25



January 26



February 26



March 26



April 26



Tower M5

TOWER STATUS

- Terrace Floor Slab works in progress.
- 3rd Floor Internal Gypsum Plaster in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- 12th Floor Slab Completed.
- Internal Gypsum Plaster till 2nd Floor Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Terrace Floor Slab.

PROGRESS TIMELINE



November 25



December 25



January 26



February 26



March 26



April 26



Tower P1

TOWER STATUS

- Pour 01 8th Floor Slab in progress and Pour 02 5th Floor Slab in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Excavation Completed.
- Foundation Completed.
- Pour 01 7th Floor Slab & Pour 02 4th Floor Slab Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of 5th & 8th Floor Slab.

PROGRESS TIMELINE



December 25



January 26



February 26



March 26



April 26



Tower M7

TOWER STATUS

- Stilt Floor Slab works completed.
- 2nd Floor Slab works in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Excavation Completed.
- Foundation Completed.
- Stilt Slab Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of 3rd Floor Slab..

PROGRESS TIMELINE



January 26



February 26



March 26



April 26



Tower M6

TOWER STATUS

- Tower M6 Stilt Floor works in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Excavation Completed.
- Foundation Completed.
- Plinth Works Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Stilt Slab.

PROGRESS TIMELINE



February 26



March 26



April 26


MLCP 1



TOWER STATUS

- Pour 01 & Pour 02 Terrace Slab Completed.
- Pour 03 Excavation in Progress.

Internal Finishes - Tiling

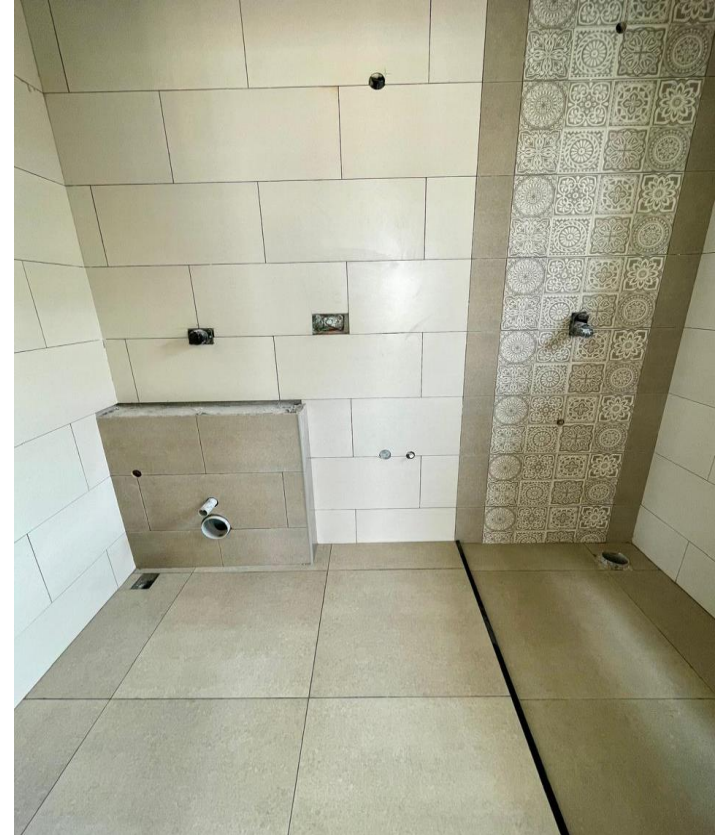

TOWER STATUS

- Tower K Completed.
- Tower M3 Completed.
- Tower M1 Completed..
- Tower P4 Completed.
- Tower M2 5th to 7th Floor in Progress.
- Tower E15 10th Floor in Progress.
- Tower L 1st to 4th Floor in Progress.
- Tower P3 1st to 4th Floor in Progress.
- Tower P2 1st & 2nd Floor in Progress.

Internal Finishes - Joinery



TOWER STATUS - WINDOWS

- Tower K 7th to 9th Floor in Progress.
- Tower M3 Completed.
- Tower P4 7th to 10th Floor in Progress.
- Tower M1 5th to 7th Floor in Progress.
- Tower E15 All Floors in Progress.

TOWER STATUS - DOORS

- Tower K 7th & 8th Floor in Progress.
- Tower M3 Completed.
- Tower P4 6th Floor in Progress.
- Tower M1 5th to 7th Floor in Progress.
- Tower E15 1st Floor in Progress.

Contact us

Site Office :

No: 14 Surya Nagar, Erikarai Road,
Pallikaranai, Chennai - 600100.

Regional Office :

Puravankara Limited. #130/1, Ulsoor Road,
Bengaluru - 560 042

Email : crm@puravankara.com (Subject line – Project name/ unit number)

Call Us : +91 - 80-67724001 / 1 860 208 0000

Web : www.puravankara.com

RERA Registration Number :

RERA No: TN/29/BUILDING/0008/2023 | TN/29/BUILDING/0009/2023 |
TN/29/BUILDING/0010/2023
